


Project: Grippler Hangers
Client: Grippler Ltd
Client's Order No: 3061
Inspection Date:
First: 12/03/2009

Certificate No: COV 0919097
Office: Sheffield
Date: 20/02/2009
Order Status: Complete
Final: 12/03/2009

This certificate is issued to Grippler Ltd to certify that the undersigned surveyor did, at their request attend their premises at The Old West Gun Works, Sheffield on and between the above dates for the purpose of examining and witnessing tests on the items listed below. All tests produced satisfactory results.

TEST CONFIGURATION

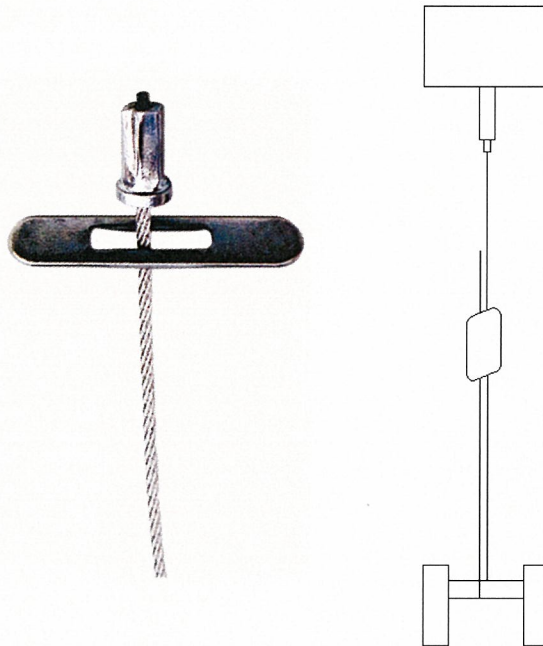

M Cobb
Surveyor of Lloyd's Register



Grippler Model	Rope Construction	Grippler Rated Load	Grippler Load Limit 5:1	Result		
No.4 Toggle	7x19 (6/1)	90-225 kg 198-495 lbs	1125kg 2475 lbs	1498.3 kg 3296.3 lbs	1554.5 kg 3412 lbs	1552.2 kg 3415 lbs



CABLE JOINTS, CABLE TERMINATIONS, CABLE GLANDS, CABLE CLEATS
FEEDER PILLARS, FUSE LINKS, ARC FLASH, CABLE ROLLERS, CUT-OUTS

11KV 33KV CABLE JOINTS & CABLE TERMINATIONS
FURSE EARTHING
www.cablejoints.co.uk
Thorne and Derrick UK
Tel 0044 191 490 1547 Fax 0044 191 477 5371
Tel 0044 117 977 4647 Fax 0044 117 9775582
