


Project: Gripple Hangers
Client: Gripple Ltd
Client's Order No: 8624
Inspection Date:
First: 19/12/2007

Certificate No: COV 0719796
Office: Sheffield
Date: 19/01/2008
Order Status: Complete
Final: 21/01/2008

This certificate is issued to Gripple Ltd to certify that the undersigned surveyor did, at their request attend their premises at The Old West Gun Works, Sheffield on and between the above dates for the purpose of examining and witnessing tests on the items listed below. All tests produced satisfactory results.

TEST CONFIGURATION

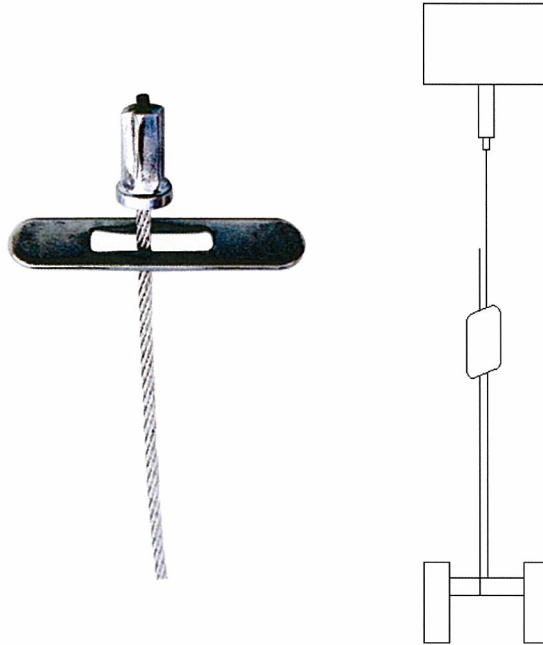

M Cobb
 Surveyor of Lloyd's Register

WITNESSED / REVIEWED
 Lloyd's Register
 EMEA
 26/1/08

Gripple Model	Rope Construction	Gripple Rated Load	Gripple Load Limit 5:1	Result		
No.1 Toggle	7x7 (6/1)	0 - 10 kg 0 - 22 lbs	50kg 110 lbs	84.0 kg 184.8 lbs	85.4 kg 187.8 lbs	55.8 kg 122.8 lbs
No.2 Toggle	7x7 (6/1)	10 - 45 kg 22 - 100 lbs	225kg 500 lbs	289.8 kg 637.6 lbs	291.9 kg 642.2 lbs	263.2 kg 579.0 lbs
No.3 Toggle	7x7 (6/1)	45 - 90 kg 100 - 200 lbs	450 kg 990 lbs	537.8 kg 1183.2 lbs	536.0 kg 1179.2 lbs	507.9 kg 1117.4 lbs



CABLE JOINTS, CABLE TERMINATIONS, CABLE GLANDS, CABLE CLEATS
FEEDER PILLARS, FUSE LINKS, ARC FLASH, CABLE ROLLERS, CUT-OUTS

11KV 33KV CABLE JOINTS & CABLE TERMINATIONS

FURSE EARTHING

www.cablejoints.co.uk

Thorne and Derrick UK

Tel 0044 191 490 1547 Fax 0044 191 477 5371

Tel 0044 117 977 4647 Fax 0044 117 9775582
